



SUB 3[®]

Global Program Portfolio Management Consultants

8 Weeks to Success with Oracle Primavera P6

SUB3 Management Inc.

8 Weeks to Success with Oracle Primavera P6

Maximize your software investment with SUB3's "8 Weeks to Success with Oracle Primavera P6"

8 Weeks to Success with Oracle Primavera P6

- Objectives
- SUB3 Implementation Methodology
- SUB3 Implementation Methodology Phases

Objectives

8 Weeks to Success with Oracle Primavera P6

- Oracle Primavera P6 up and running in eight weeks
- Develop an environment to sustain growth of P6
- Provide an integration Work Group to consider future integration (of necessary)
- Lessons Learned and Closeout Work Group

SUB3 Implementation Methodology

	Discovery - Requirements	Design & Configuration Work Groups	Pilot Test	Deploy	Lessons Learned & Closeout Work Group
Resources	<ul style="list-style-type: none"> ➤ Sponsor ➤ Project Manager ➤ Core Team, 	<ul style="list-style-type: none"> ➤ Project Manager ➤ Core Team ➤ Business Users ➤ Technical 	<ul style="list-style-type: none"> ➤ Core Team ➤ Business Users ➤ Administration 	<ul style="list-style-type: none"> ➤ Business Users ➤ Core Team ➤ Administration 	<ul style="list-style-type: none"> ➤ Sponsor ➤ Project Manager ➤ Core Team ➤ Business Users ➤ Technical
Steps	<ul style="list-style-type: none"> ➤ Requirements Review ➤ Current State ➤ Future State ➤ Data Flows ➤ Process Review 	<ul style="list-style-type: none"> ➤ Core Team Training ➤ Integration Work Group 	<ul style="list-style-type: none"> ➤ Review current process / procedures ➤ Execute Test Plan ➤ Review Production Readiness ➤ Review / Finalize Issues Log 	<ul style="list-style-type: none"> ➤ Move to Production ➤ Closeout Issues Log ➤ Additional User Training 	<ul style="list-style-type: none"> ➤ Collect Lessons Learned Artifacts
Output	<ul style="list-style-type: none"> ➤ Project Plan ➤ Testing Plan ➤ Training Plan ➤ Environment Questionnaire ➤ Risk Review 	<ul style="list-style-type: none"> ➤ Configuration Document ➤ Integration High-Level Requirements 	<ul style="list-style-type: none"> ➤ User Training ➤ Signoff - Production Readiness 	<ul style="list-style-type: none"> ➤ Production System Turnover ➤ Post Implementation Review ➤ Final Issues Log 	<ul style="list-style-type: none"> ➤ Lessons Learned ➤ Next Steps ➤ Recommendations ➤ Final Signoff

Discovery/Requirements

8 Weeks to Success with Oracle Primavera P6

- Kickoff Meeting – Including:
 - Project Sponsor
 - Project Manager
 - Core Team
 - SUB3 Resources
- Review Steps –
 - Requirements
 - Data Flows
 - Current/Future State
 - Process/Procedures
- Develop the project plan for the implementation
- Initiate Risk Review with follow-up at each phase

Design & Configuration Work Groups

8 Weeks to Success with Oracle Primavera P6

- Core Team with Business Users input design and configure P6
- Configuration Document captures all decisions and assumptions
- Determine if desk instructions/user guides will be developed
- Initial discussion of Integration Requirements documented into high level specification document

Pilot Test

8 Weeks to Success with Oracle Primavera P6

- Business Users Trained
- Administrator Trained
- Business Users with Core Team Support test the system using the Test Plan
- Determine if desk instructions/user guide modifications are necessary
- Signoff for Production Readiness

Deploy

8 Weeks to Success with Oracle Primavera P6

- Core Team turns over Production System to Business Users
- Administrator signs off on User Profiles, Security, etc.
- P6 moved to Production
- Determine if additional users need to be trained
- Issues Log Signed off (Finalized)
- Post Implementation Review


Lessons Learned & Closeout Work Group

8 Weeks to Success with Oracle Primavera P6

- Lessons Learned Work Group
 - Output provided to Management and Core Team
- Next Steps and Recommendations document completed and submitted
- Final Assessment & Review of all output
- Final Signoff

Sample Project Schedule

8 Weeks to Success with Oracle Primavera P6

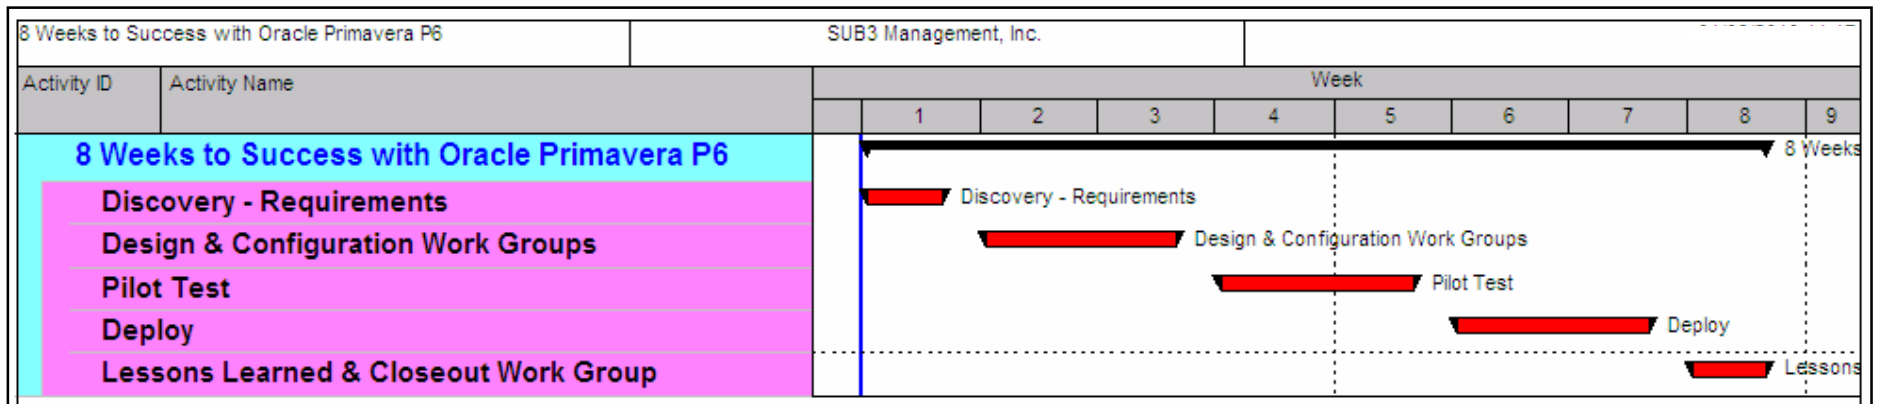

Additional Information

8 Weeks to Success with Oracle Primavera P6

- Additional Information

SUB3 Management, Inc.

info@sub3mgmt.com

866.505.7823

www.sub3mgmt.com
